PROJECT PLANNING/SCHEDULE

Client Name :

Project Name :

Project Manager / Team Leader :

Project Start Date :

Project End Date :

Project Length in Days :

Modified of Renovation and additional construction of RR nagar constituency MLA office, BBMP RR Nagar Division Executive engineer and Yeshwanthapura Sub Division Assistant Executive engineer office behind Chowdeshwari Bus stop, J P Park and construction of compound wall in front of J P Park in Ward no.17

30-Aug-19
29-Aug-20
365

Sl. No	Assignment	Unit	Req. Qty/hr	Start Date	End Date	No. of Working Days
1	Dismantling of existing structures like culverts, bridges, retaining walls and other structures comprising of masonry.	Cum	47.80	4-Sep-19	4-Oct-19	30
2	Dismantling segmental arches in the lintels with small wall including foundation and bearing etc., including stacking the	Rmt	1357.50	5-Sep-19	23-Sep-19	20
3	Dismantling plastering and removing the defects with a hard type, Mines including cost of materials., Ceiling Etc.Out	Sqm	344.40	7-Sep-19	17-Sep-19	10
4	Dismantling mosaic/tiled roadways in cha/ourries, lime mixing, removal existing and stacking the bricks within a radius	Cum	13.00	9-Sep-19	19-Sep-19	10
5	Dismantling concrete/concrete flooring or plain concrete concrete work including removing and transporting the debris to	Sqm	363.00	11-Sep-19	11-Sep-19	10
6	Removing of existing old wooden Window/door frames / Shutters and Openings with all cost and conveyance lifting to	Each	2.00	13-Sep-19	23-Sep-19	10
7	Dismantling the tar work in floor and road mat as external or wide course including stacking the materials with in 50 m lead	Sqm	651.00	15-Sep-19	23-Sep-19	8
8	Dismantling of existing structures like culverts, bridges, retaining walls and other structures comprising of masonry.	MT	6.00	17-Sep-19	27-Sep-19	10
9	Dismantling of ground slab by manual means and disposal of dismantled materials with all lifts and stacking serviceable	Each	60.00	19-Sep-19	29-Sep-19	10
10	Earth work exc.Conveying & unloading the ground other than ordinary soil in Mechanical means upto 3.0 mts depth	Cum	168.00	20-Sep-19	30-Oct-19	20
11	SOR 3.2.1 Earthwork excavation for Foundation of buildings, culverts, water supply, sanitary lines and electrical	Cum	1012.19	22-Sep-19	12-Oct-19	20
12	Construction of embankment with approved material (Granite/ Murrum) with all lifts and leads, transporting to site,	Cum	268.00	24-Sep-19	14-Oct-19	20
13	Providing and laying in position plain cement concrete of mix 1:5:10 with OPC cement @ 250kgs. with 40mm and down size	Cum	150.40	25-Sep-19	9-Oct-19	10
14	SOR 9.1.2. Providing and laying in position plain cement concrete of mix M15 with cement @ 300kgs. with 20mm and	Cum	38.20	1-Oct-19	11-Oct-19	10
15	Providing & laying 2% POSITION REINFORCED CEMENT CONCRETE of design mix M20 with OPC	Cum	722.50	6-Oct-19	5-Nov-19	30
16	Providing & laying 2% POSITION REINFORCED CEMENT CONCRETE of design mix M25 with OPC	Cum	48.00	20-Oct-19	19-Nov-19	30
17	Providing cost concreting, centering, shuttering, finishing, curing etc., as external of foam work for Foundation	Sqm	464.50	5-Oct-19	4-Nov-19	30
18	Providing cost concreting, centering, shuttering, finishing, curing etc., as external of foam work for sides & soffits of	Sqm	1099.70	10-Oct-19	24-Nov-19	45
19	Providing cost concreting, centering, shuttering, finishing, curing etc., as external of foam work for sides & soffits of	Sqm	237.00	15-Oct-19	29-Nov-19	45
20	Providing cost concreting, centering, shuttering, finishing, curing etc., and external of foam work for sloping ot	Sqm	774.33	20-Oct-19	7-Dec-19	48
21	Providing cost concreting, centering, shuttering, finishing, curing etc., and external of foam work for flat surface such	Sqm	23.00	25-Oct-19	10-Dec-19	46
22	Providing cost concreting, centering, shuttering, finishing, curing etc., and external of foam work for flat surface such	Sqm	163.00	30-Oct-19	4-Dec-19	35
23	Providing cost concreting, centering, shuttering, finishing, curing etc., for columns, pillars, piers, abutments, post and	Sqm	435.75	4-Nov-19	4-Dec-19	30
24	Providing cost concreting, centering, shuttering, finishing, curing etc., for columns, pillars, piers, abutments, post and	Sqm	30.00	5-Nov-19	5-Dec-19	30
25	Providing and laying in position cost/carrol cement concrete of design mix M20 with OPC cement @ 2" 20 Kgs with 12mm	Sqm	33.00	25-Nov-19	15-Dec-19	20
26	Providing cost concreting, centering, shuttering, finishing, curing etc., for Chajjas, corbels of all shapes & sizes, at all	Sqm	14.00	27-Nov-19	12-Dec-19	15
27	Providing cost concreting, centering, shuttering, finishing, curing etc., for Chajjas, corbels of all shapes & sizes, at all	Sqm	5.00	29-Nov-19	14-Dec-19	15
28	Providing cost concreting, centering, shuttering, finishing, curing etc., and external of foam work for slaves (including landing)	Sqm	14.00	1-Dec-19	16-Dec-19	15
29	Providing TMT bars reinforcement for RCC works including straightening, cutting, bending, bending, placing in position	MT	61.74	3-Oct-19	18-Oct-19	15
30	Providing TMT bars reinforcement for RCC works including straightening, cutting, bending, bending, placing in position	MT	6.00	5-Oct-19	4-Nov-19	30
31	SOR 9.3.5. Providing and constructing grease / trap / found size waste masonry in basement with cement mortar 1:6,	Cum	167.08	6-Oct-19	21-Oct-19	15
32	Providing and constructing foam brick masonry with approved quality of coreblow bricks of standard size of class	Cum	23.70	7-Oct-19	22-Oct-19	15
33	Providing and constructing foam brick masonry with approved quality of coreblow bricks of standard size of class	Cum	41.60	6-Dec-19	24-Dec-19	20
34	Providing and constructing foam brick masonry with approved quality of coreblow bricks of standard size of class	Cum	14.00	18-Dec-19	7-Jan-20	20
35	Construction of partition wall 11.2 cm thick with cm coreblow table moulded foam bricks of class designation	Sqm	52.00	9-Dec-19	3-Jan-20	25
36	Construction of partition wall 11.2 cm thick with cm coreblow table moulded foam bricks of class designation	Sqm	13.00	23-Dec-19	17-Jan-20	25
37	SOR 9.15. Providing and constructing load bearing wall with concrete concrete solid blocks having block density not	Sqm	340.40	19-Dec-19	4-Jan-20	25
38	Providing & constructing non load bearing walls with solid concrete blocks of size 400x200x200 having block density not	Sqm	107.20	13-Dec-19	7-Jan-20	25
39	Providing 10mm thick cement plaster in single coat with cement mortar 1:3 to Brick masonary including rounding off	Sqm	496.30	7-Dec-19	1-Jan-20	25
40	Providing 10mm thick cement plaster in single coat with cement mortar 1:3 to Brick masonary including rounding off	Sqm	166.30	13-Dec-19	9-Jan-20	25
41	Providing 10mm thick cement plaster in single coat with cement mortar 1:3 to Brick masonary including rounding off	Sqm	132.00	9-Dec-19	8-Jan-20	30
42	Providing 10mm thick cement plaster in single coat with cement mortar 1:4, to brick masonary including rounding off	Sqm	1300.10	14-Dec-19	13-Jan-20	30

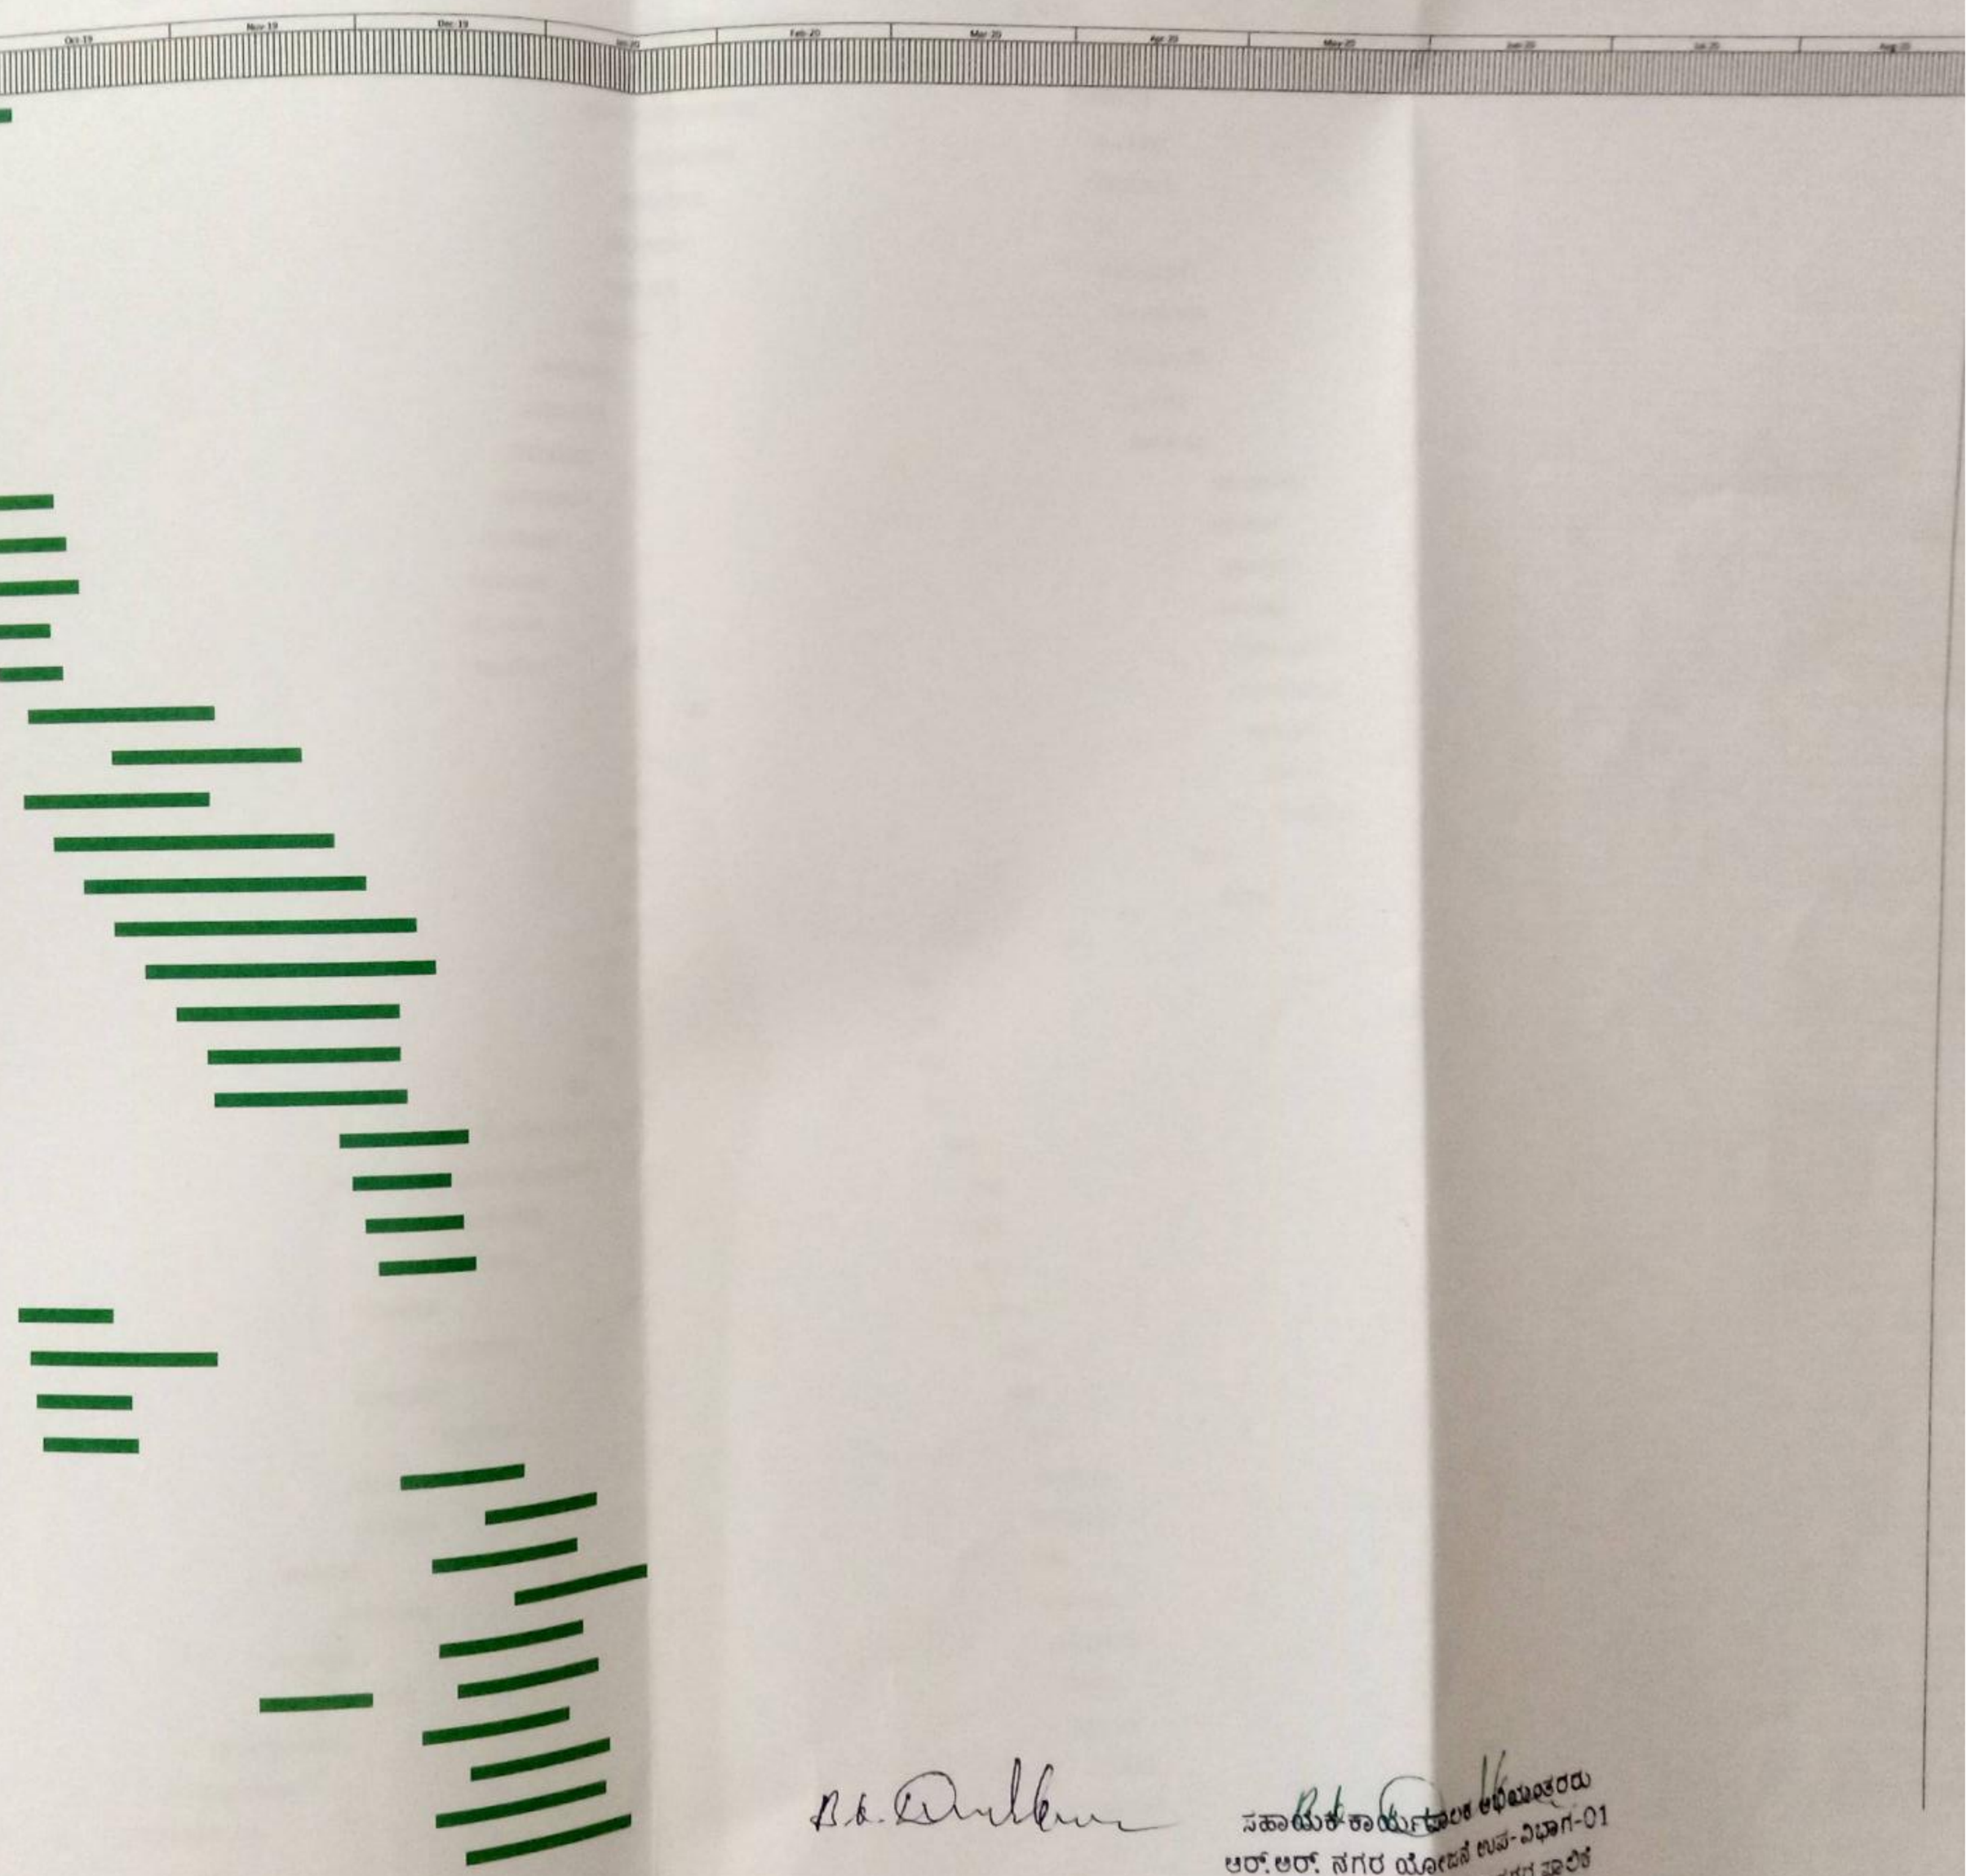

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಆರ್.ಆರ್. ನಗರ ಯೋಜನೆ ಉಪ-ವಿಭಾಗ-01
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

Scanned by TapScanner

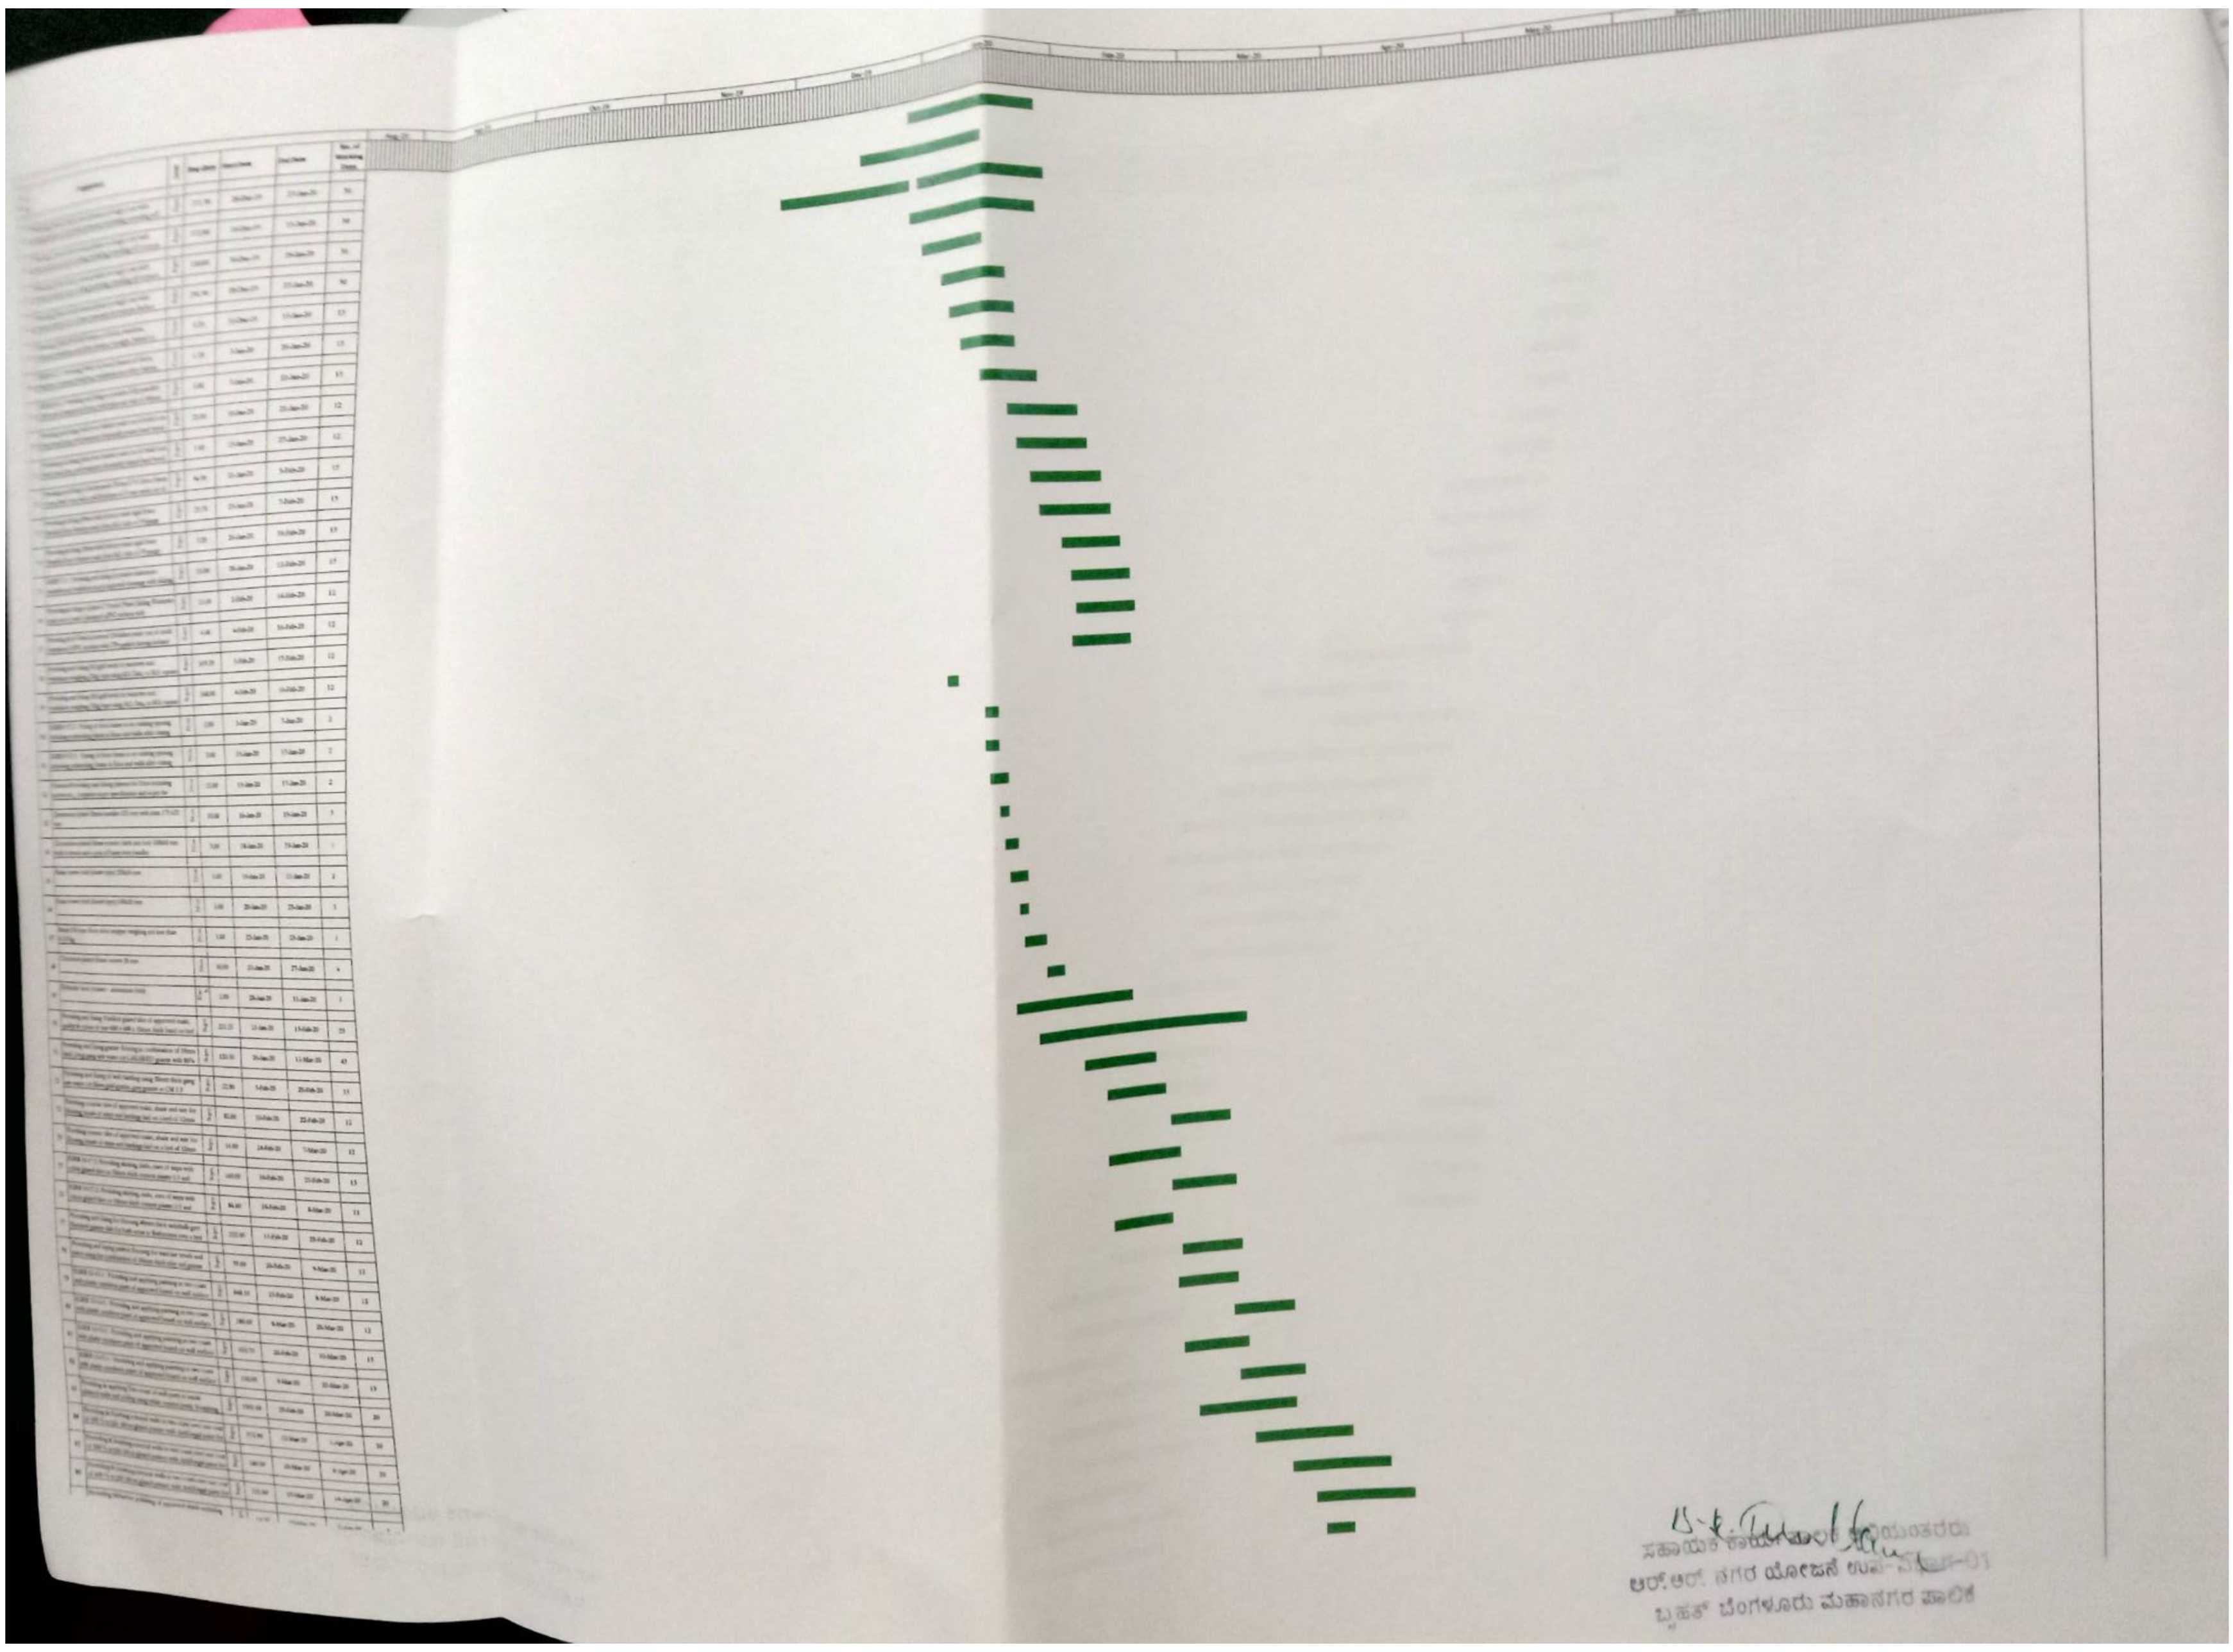

Scanned by TapScanner

Scanned by TapScanner

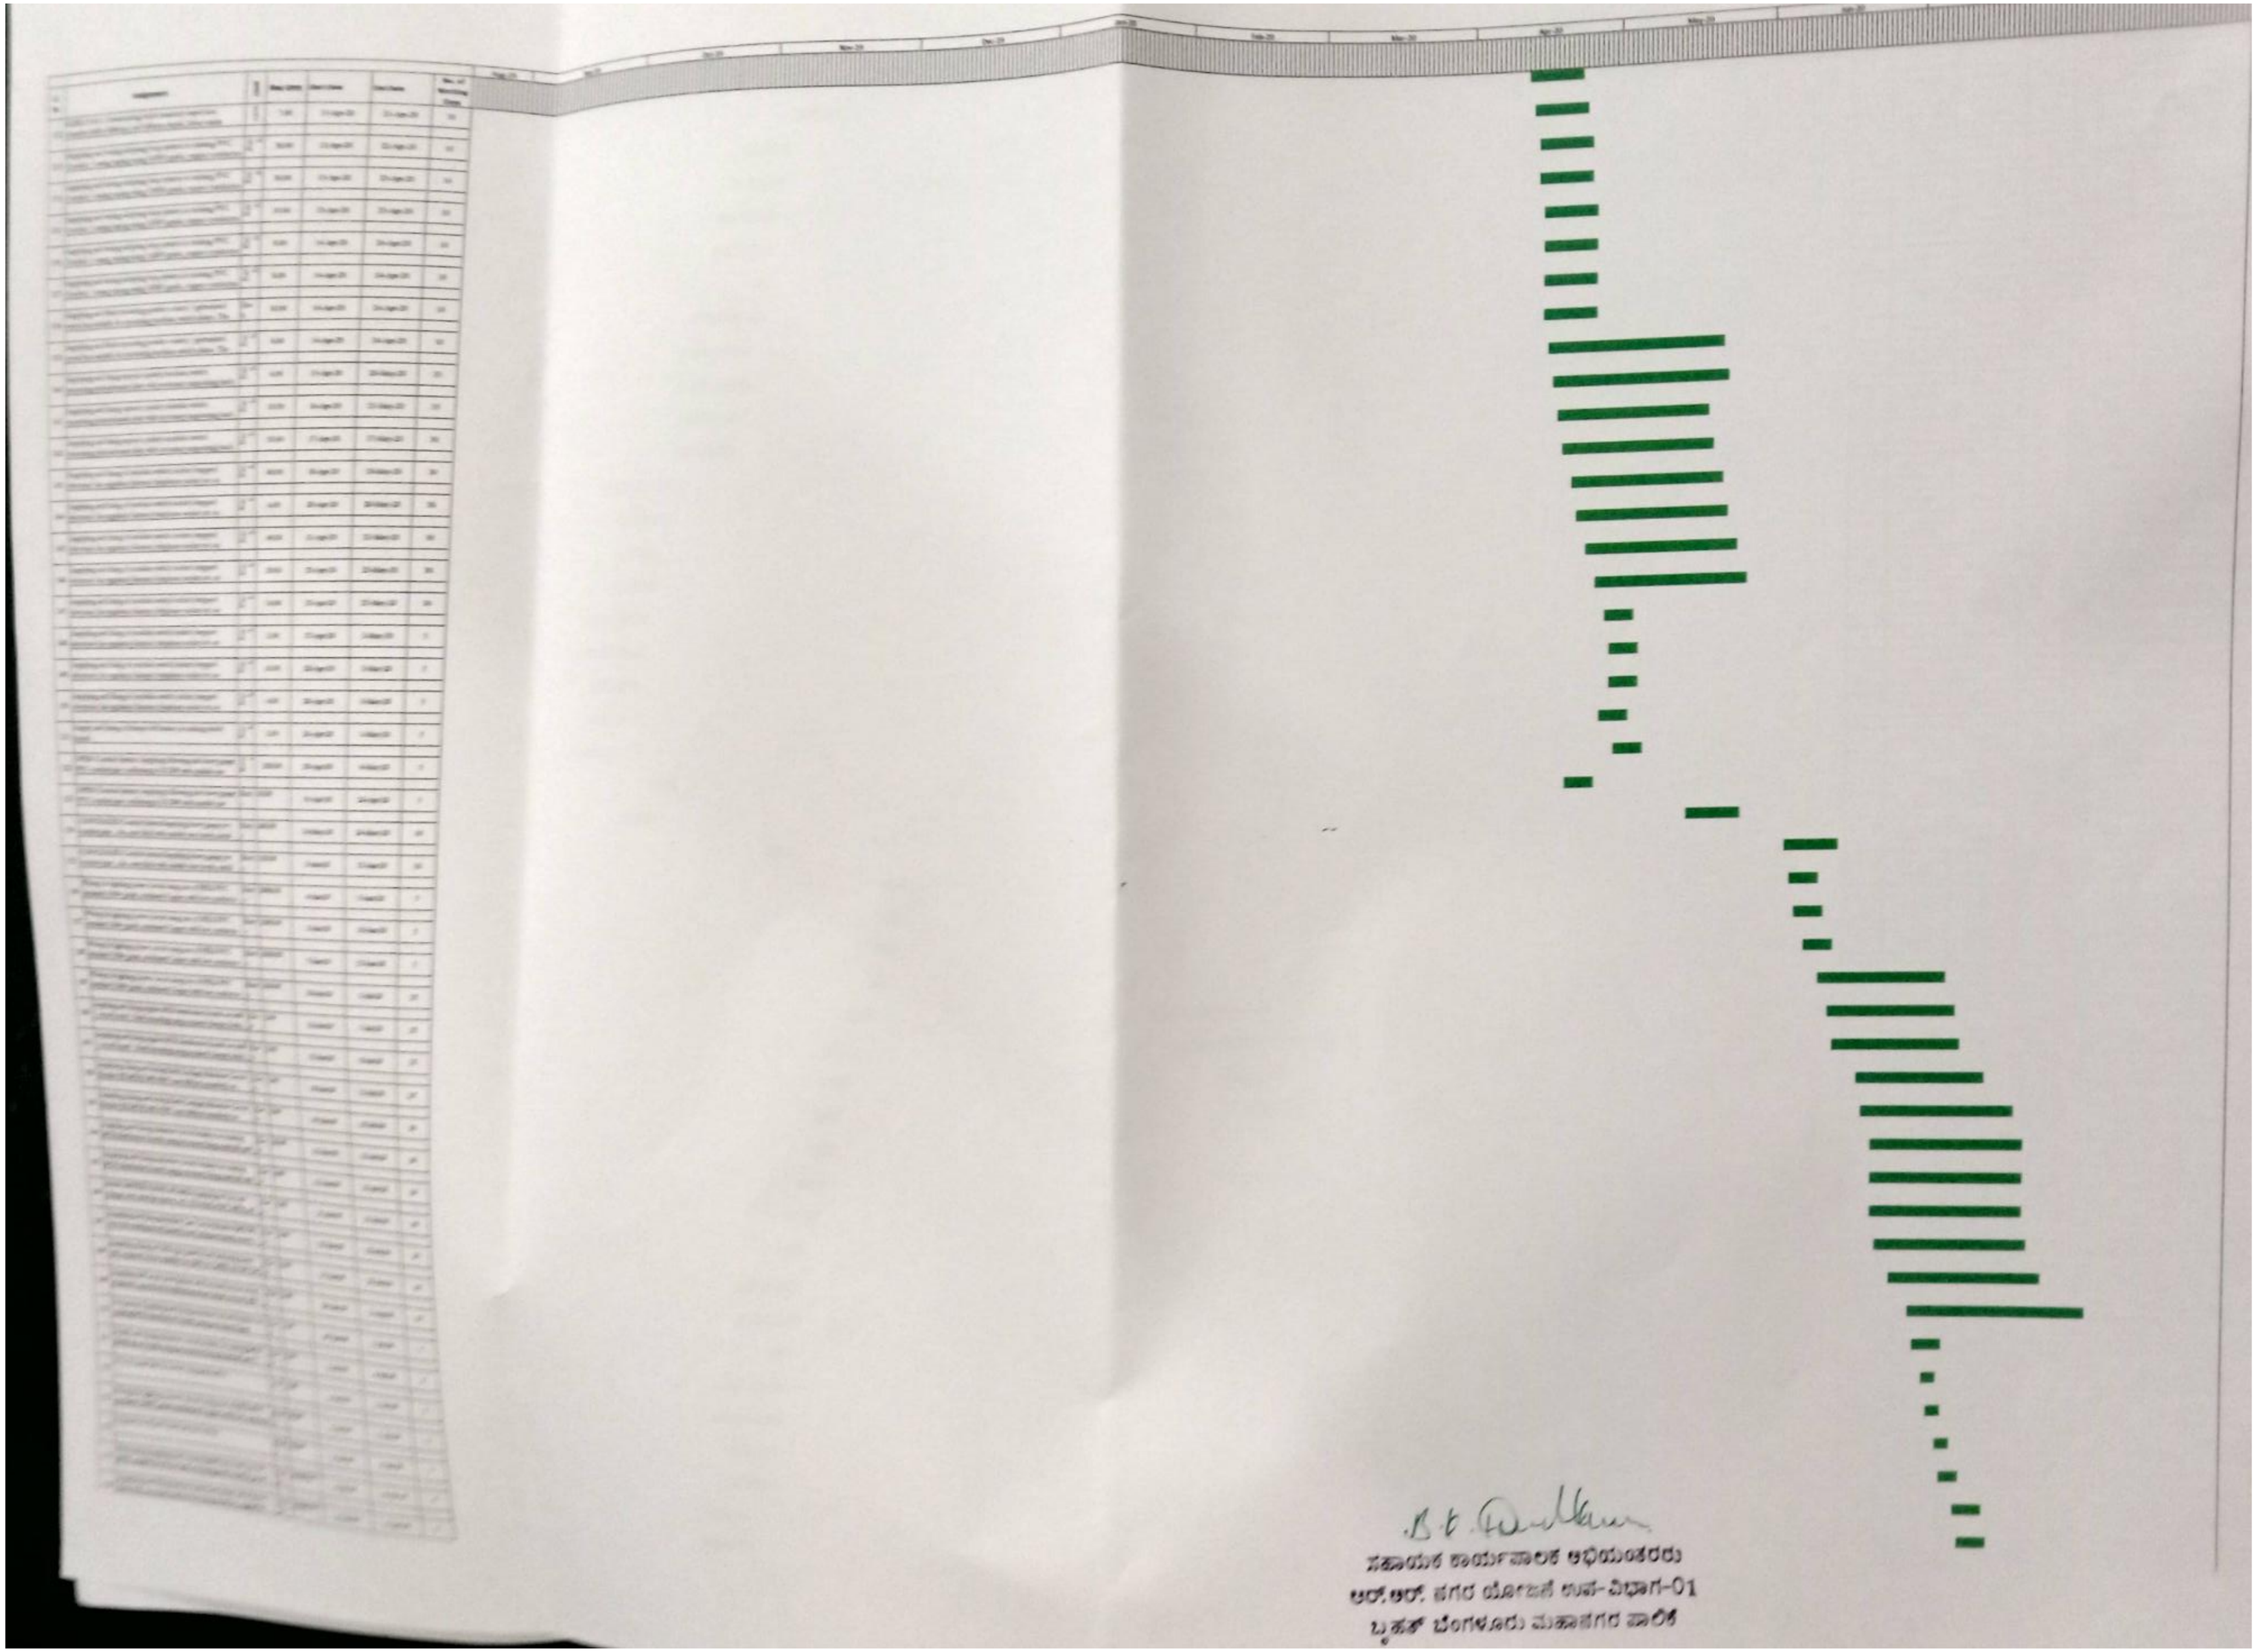

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಆರ್.ಆರ್. ನಗರ ಯೋಜನೆ ಉಪ-ವಿಭಾಗ-01
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

Scanned by TapScanner

	Assignment	Unit	Req. Qnty	Start Date	End Date	No. of Working Days
		Each	50.00	16-Jul-20	13-Jul-20	3
		Each	20.00	16-Jul-20	15-Jul-20	3
		Each	30.00	11-Jul-20	16-Jul-20	3
		Each	8.00	12-Jul-20	17-Jul-20	3
		Each	8.00	14-Jul-20	17-Jul-20	3
42	Supplying of 1440rpm heavy duty exhaust fan with louvher blades suitable for operate on 230V 50Hz, AC Supply	Each	2.00	16-Jul-20	19-Jul-20	3
43	Supplying capacitor type 48" sweep ceiling fan complete with plates and blades, shackle, canopies etc., for operation on 230	Each	4.00	19-Jul-20	22-Jul-20	3
44	Supplying wall mounting fan suitable to operate at single phase 230V AC Supply 400mm sweep	Each	2.00	20-Jul-20	23-Jul-20	3
45	Fixing all types and all capacities fluorescent / false ceiling flood light / CFL(6/8/9/12/18/24watts) indoor on the wall	Each	52.00	21-Jul-20	24-Jul-20	3
46	Fixing x-ceiling/ Wall mounting fan of all capacities and all types to the existing U hook together with supplying and fixing	Each	8.00	22-Jul-20	27-Jul-20	5
47	Supplying & fixing cast iron clutch GI pipe bracket up to 2 meters long terminated with a reducing collar of 40x25mm	Each	5.00	23-Jul-20	28-Jul-20	5
48	Supplying of 1.5TR Split air conditioners suitable for operation on AC Supply Single phase 50Hz 230 Volts	Each	2.00	23-Jul-20	28-Jul-20	5
49	Supply erection, testing, commissioning of Cassete type Split Air conditioners suitable for operation on AC Supply Single	Each	1.00	24-Jul-20	27-Jul-20	3
50	Supplying and drawing PVC Flexible one pair telephone interconnect tinned copper cable - 3 Pair	Rmtr	300.00	24-Jul-20	27-Jul-20	3
51	Supplying and drawing PVC Insulated Gas ssurred physical Foam ally Braided Co-Axial TV Cable RG-6	Rmtr	150.00	24-Jul-20	27-Jul-20	3
52	Supplying & Drawing UTP- CAT 6E-LAN Cable	Rmtr	300.00	24-Jul-20	27-Jul-20	3
53	Supplying & fixing of network switches. Supplying & Drawing UTP- CAT 6E-LAN Cable.-24 Port Gigabite (Managerable)	Each	1.00	27-Jul-20	29-Jul-20	2
54	Earthing :Supplying fixing and wiring earth electrode for grounding of transformers,HT vehicles etc using 40mm dia	Each	2.00	29-Jul-20	31-Jul-20	2
55	EARTH ITEM9- Supplying and running of GI / Copper tape for grounding conversions using necessary fixing	Rmtr	10.00	31-Jul-20	3-Aug-20	3
56	EARTH ITEM9- Supplying and running of GI / Copper tape for grounding conversions using necessary fixing	Rmtr	30.00	4-Aug-20	7-Aug-20	3
57	Supplying, erecting, testing and commissioning of voltage stabilizer suitable for 170 to 270 v as per and load variation	Each	1.00	7-Aug-20	10-Aug-20	3
58	Supplying, erecting, testing & commissioning of OFF-LINE UPS system suitable for operation on 230V, 50Hz, A/C	Each	1.00	13-Aug-20	13-Aug-20	3
59	Supplying of Fire sd box complete	Each	2.00	17-Aug-20	20-Aug-20	3
60	Provision of Solar Lighting Pnels & accessories for 5 KVA capacity	Each	1.00	22-Aug-20	25-Aug-20	3

Aug-19 Sep-19 Oct-19 Nov-19 Dec-19 Jan-20 Feb-20 Mar-20 Apr-20 May-20 Jun-20 Jul-20 Aug-20

Time Table For Work Complete

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಆರ್.ಆರ್. ನಗರ ಯೋಜನೆ ಉಪ-ವಿಭಾಗ-01
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

Scanned by TapScanner
